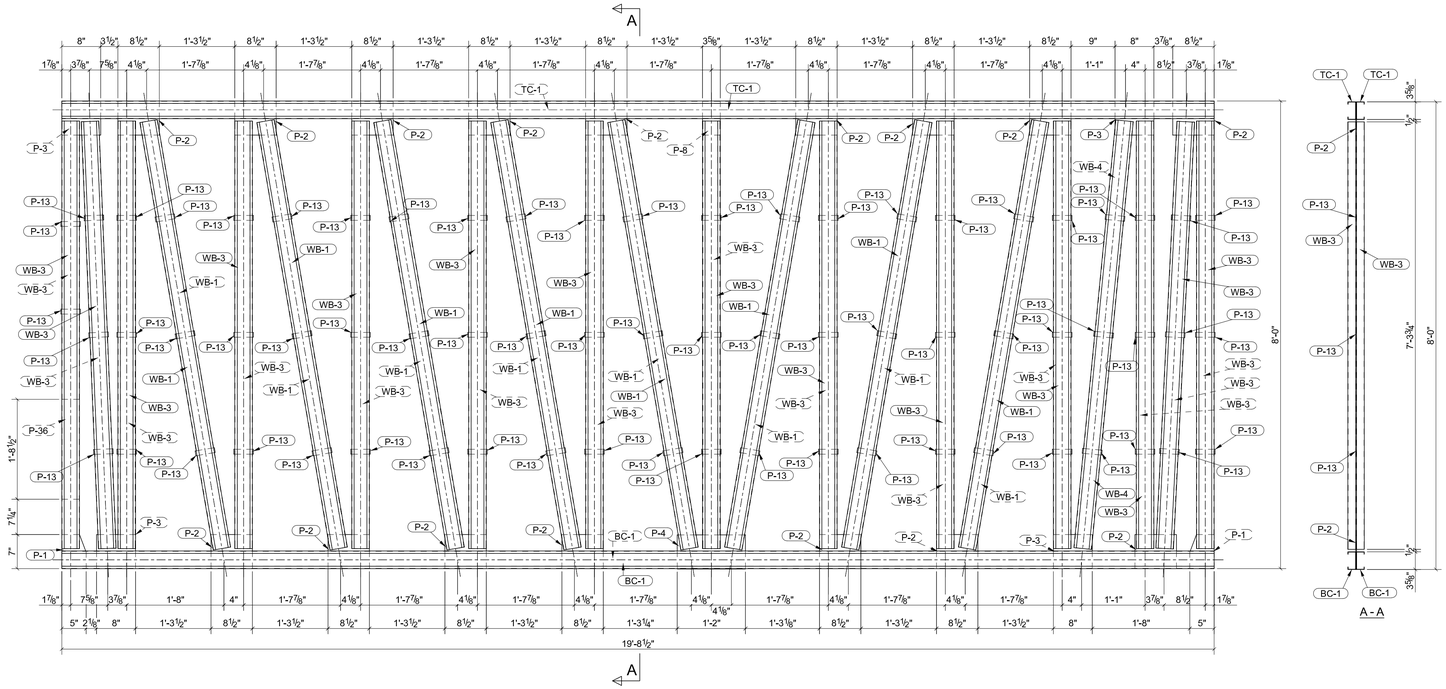



BILL OF MATERIAL

MARK	QTY	DESCRIPTION	LENGTH	WEIGHT	REMARKS
TD01	1	Truss			
TC-1	2	362S162-54	19'-8 1/2"	57	A913-50
BC-1	2	362S162-54	19'-8 1/2"	57	A913-50
P-1	2	PL1/8"X5"	0'-7"	2	A36
P-2	16	PL1/8"X7"	0'-8 1/2"	34	A36
P-3	4	PL1/8"X7"	0'-8"	8	A36
P-4	1	PL1/8"X7"	1'-2"	3	A36
P-8	1	PL1/8"X3 5/8"	0'-7"	1	A36
P-13	68	PL1/8"X1"	0'-4"	10	A36
P-36	1	PL1/8"X3 5/8"	1'-8 1/2"	3	A36
WB-1	16	362S162-54	7'-5"	170	A913-50
WB-3	28	362S162-54	7'-3 3/4"	294	A913-50
WB-4	2	362S162-54	7'-4 1/4"	21	A913-50
		TOTAL WEIGHT THIS DRAWING		659	

REV	DESCRIPTION	DATE

DESCRIPTION			
PROJECT NAME			
DRAWN BY	DZ	JOB No.	DRG No. 1
DATE DRAWN	11/29/2022		

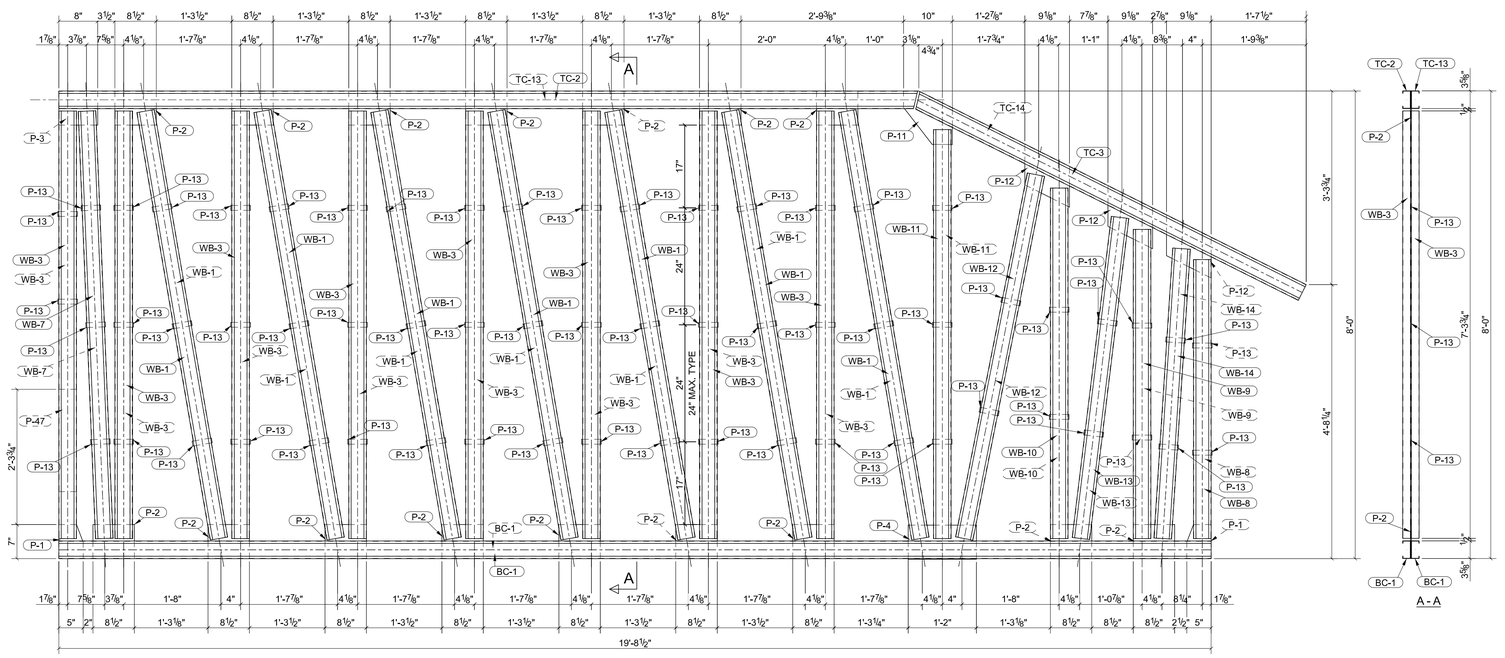











BILL OF MATERIAL

MARK	QTY	DESCRIPTION	LENGTH	WEIGHT	REMARKS
TD09	1	Truss			
TC-2	1	362S162-54	14'-8 1/4"	21	A913-50
TC-3	1	362S162-54	7'-4 5/8"	11	A913-50
TC-13	1	362S162-54	14'-8 1/4"	21	A913-50
TC-14	1	362S162-54	7'-4 5/8"	11	A913-50
BC-1	2	362S162-54	19'-8 1/2"	57	A913-50
P-1	2	PL1/8"X5"	0'-7"	2	A36
P-2	16	PL1/8"X7"	0'-8 1/2"	34	A36
P-3	1	PL1/8"X7"	0'-8"	2	A36
P-4	1	PL1/8"X7"	1'-2"	3	A36
P-11	1	PL1/8"X10"	0'-11"	3	A36
P-12	3	PL1/8"X7 1/2"	1'-2"	8	A36
P-13	62	PL1/8"X1"	0'-4"	9	A36
P-47	1	PL1/8"X3 5/8"	1'-9"	3	A36
WB-1	14	362S162-54	7'-5 1/16"	149	A913-50
WB-3	16	362S162-54	7'-3 3/4"	168	A913-50
WB-7	2	362S162-54	7'-3 13/16"	21	A913-50
WB-8	2	362S162-54	4'-9 1/4"	14	A913-50
WB-9	2	362S162-54	5'-3 7/16"	15	A913-50
WB-10	2	362S162-54	5'-11 15/16"	17	A913-50
WB-11	2	362S162-54	6'-11 15/16"	20	A913-50
WB-12	2	362S162-54	6'-4 1/8"	18	A913-50
WB-13	2	362S162-54	5'-6 7/16"	16	A913-50
WB-14	2	362S162-54	4'-11 5/8"	14	A913-50
		TOTAL WEIGHT THIS DRAWING		637	

REV	DESCRIPTION	DATE

DESCRIPTION			
PROJECT NAME			
DRAWN BY	DZ	JOB No.	DRG No.
DATE DRAWN	11/26/2022		2

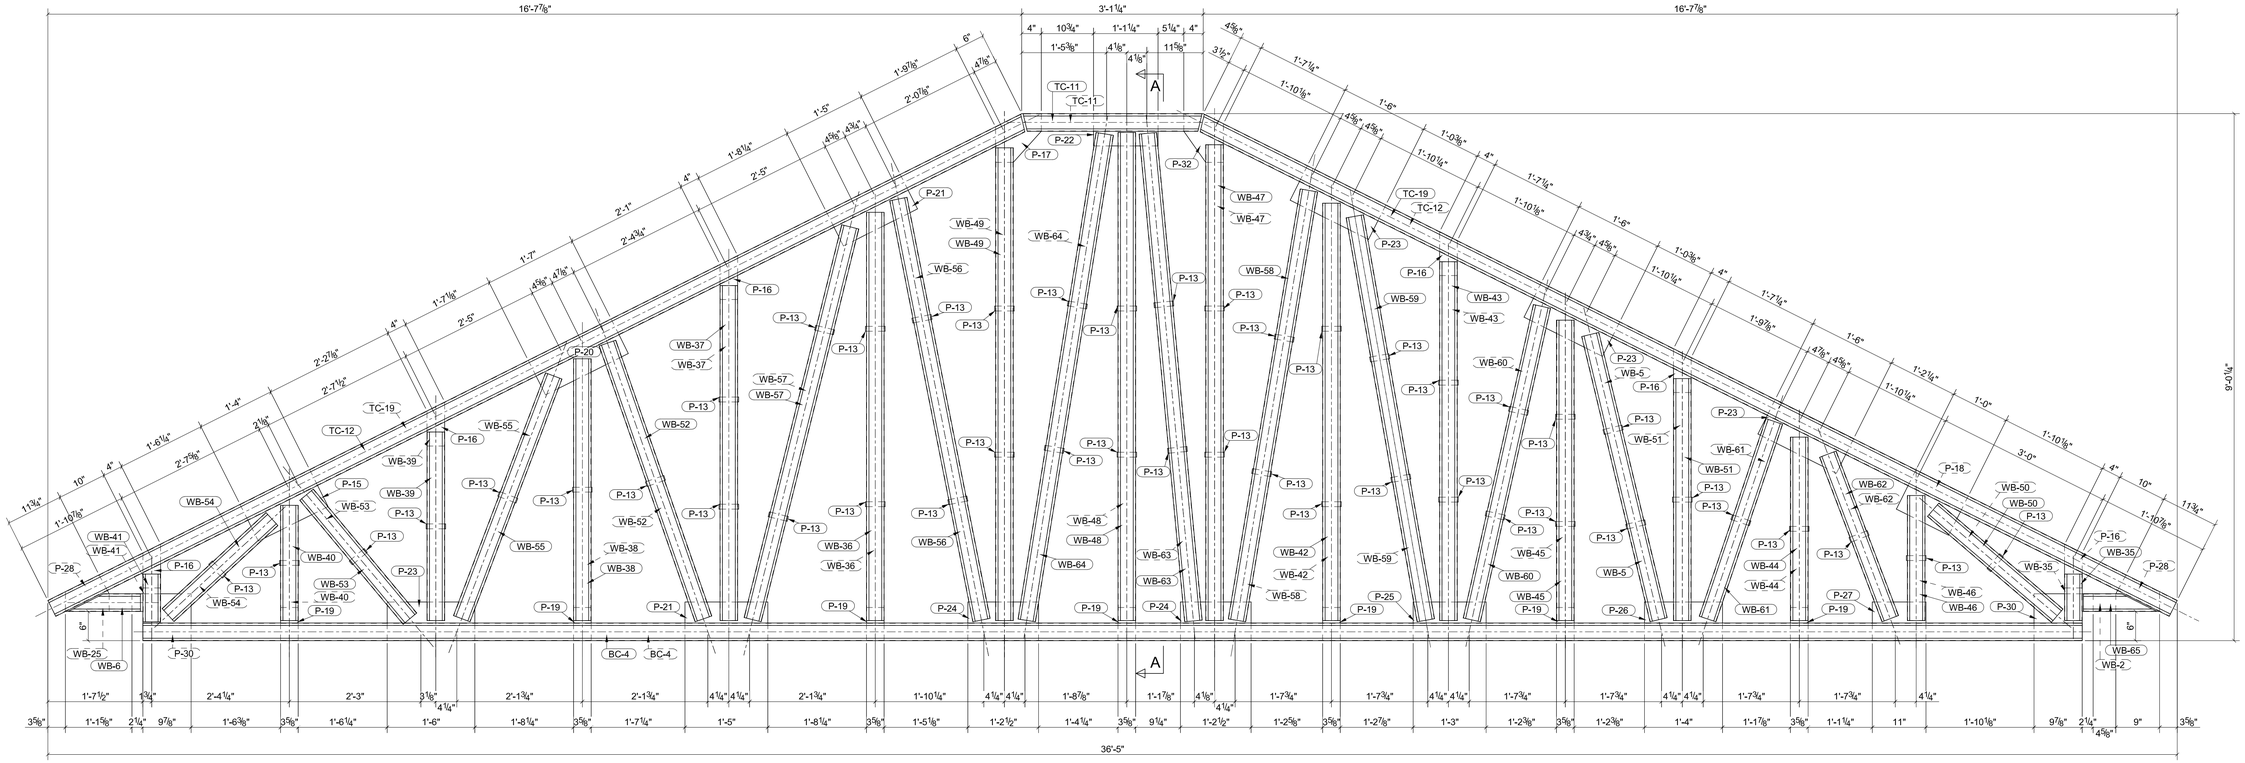

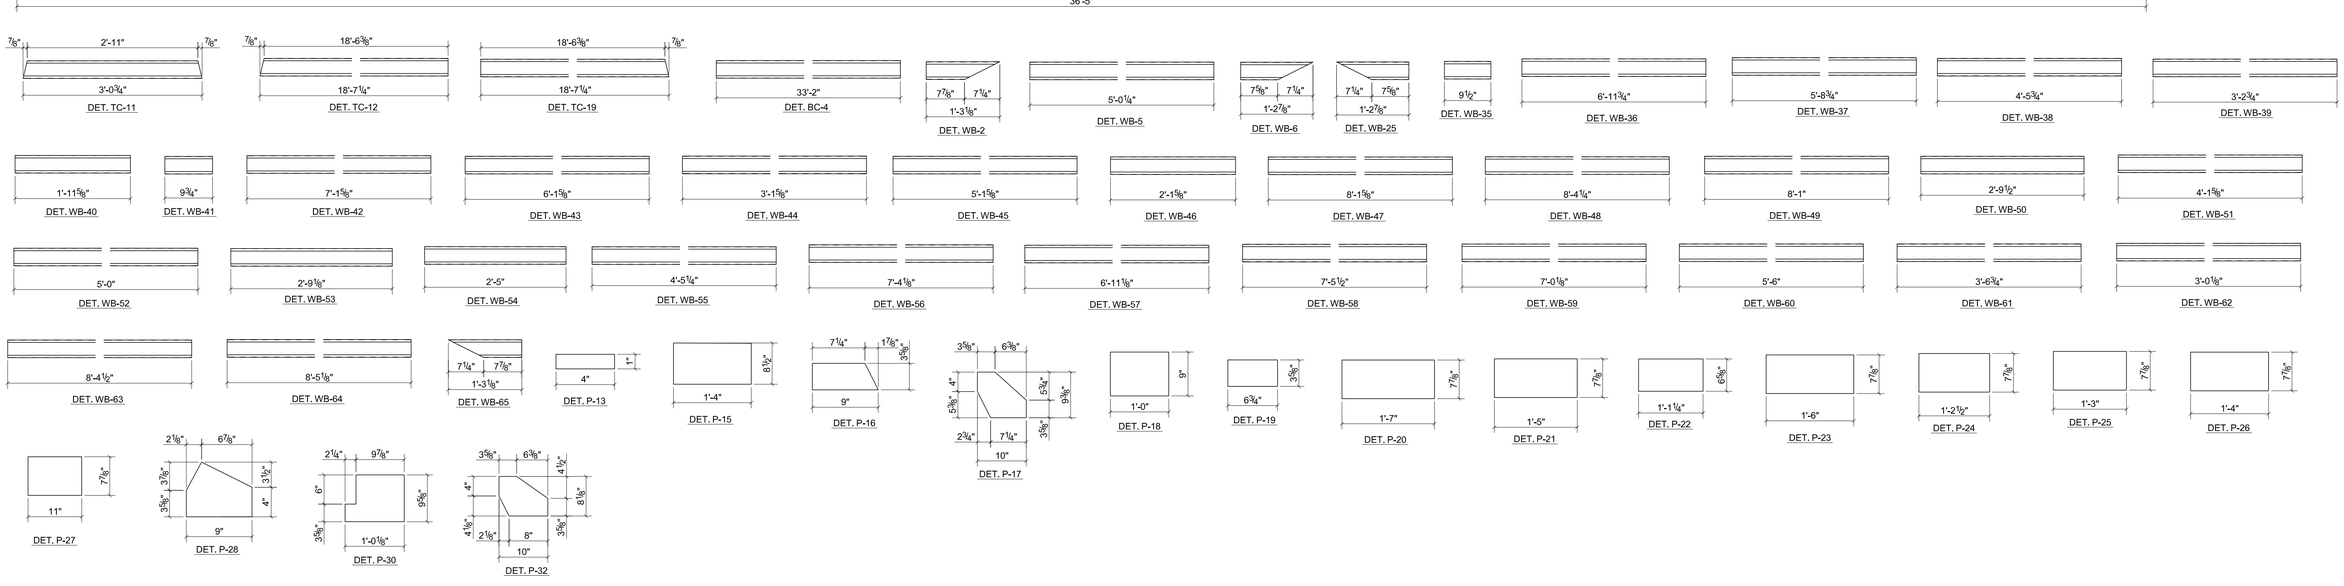

NOTE:
BILL OF MATERIAL FOR ASSEMBLY TA08 SEE SHEET 3.2

REV	DESCRIPTION	DATE

DESCRIPTION			
PROJECT NAME			
DRAWN BY	DZ	JOB No.	DRG No.
DATE DRAWN	11/26/2022		3.1

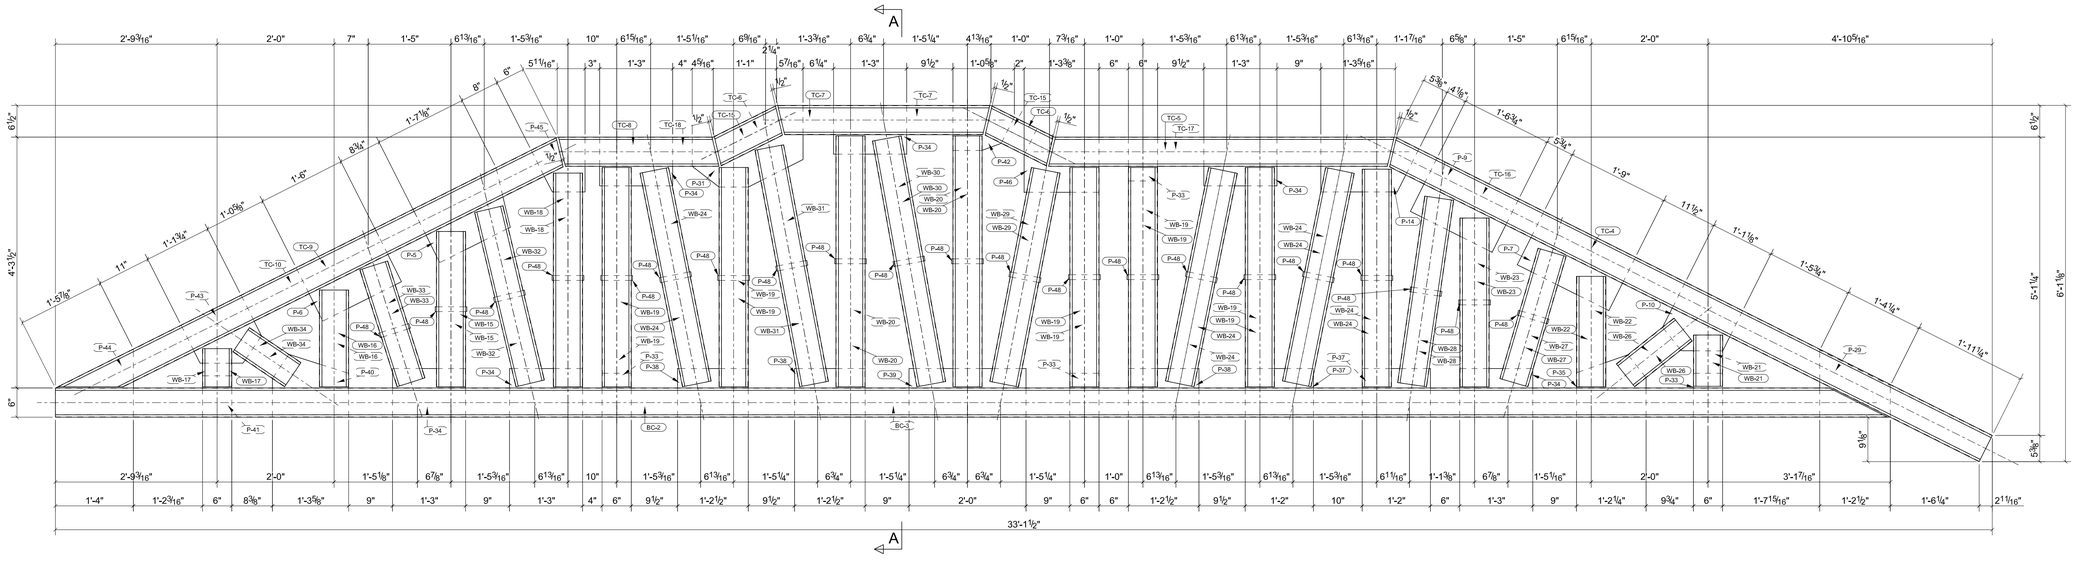

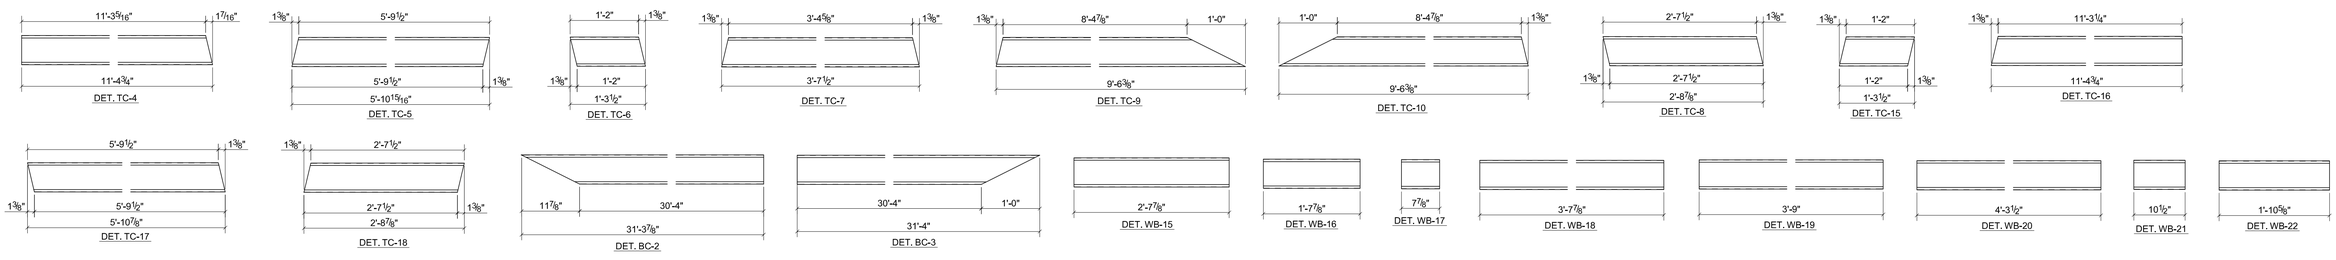

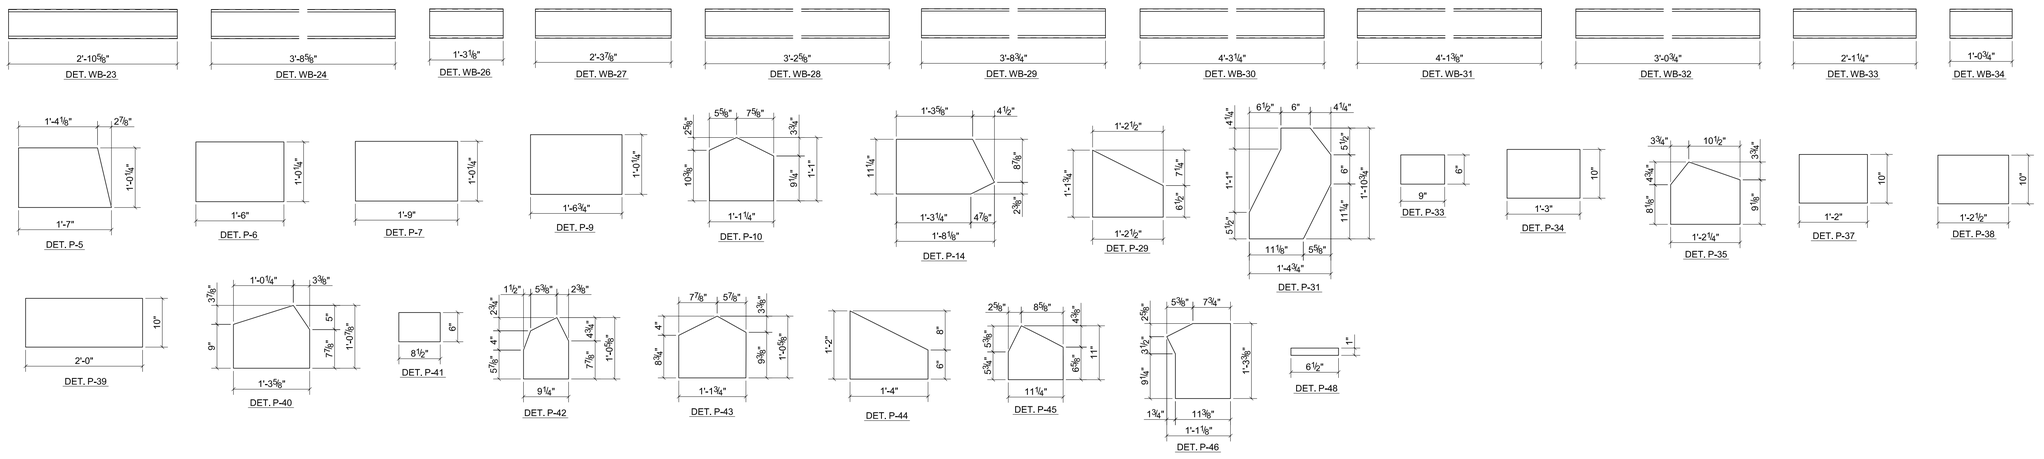

NOTE:
BILL OF MATERIAL FOR ASSEMBLY TY01 SEE SHEET 4.2

REV	DESCRIPTION	DATE

DESCRIPTION			
PROJECT NAME			
DRAWN BY	DZ	JOB No.	DRG No.
DATE DRAWN	11/26/2022		4.1
